PROVISION FOR POST PROJECT EVALUATIONS FOR THE UNITED NATIONS DEMOCRACY FUND
Contract NO.PD:C0110/10

EVALUATION REPORT

UDF-PAK-10-389 / Narrowing the Gender Gap in Flood Affected Areas of Pakistan

22 July 2014

Acknowledgements
The evaluators would like to thank everyone who took the time to provide their expertise and insight on the issues of gender and equity issues in Pakistan, and on the implementation of the project Narrowing the Gender Gap in Flood Affected Areas of Pakistan. In particular, Pattan and its partners for their support to the evaluation team during the field work.

All errors and omissions remain the responsibility of the authors.

Disclaimer
The views expressed in this report are those of the evaluators. They do not represent those of UNDEF or of any of the institutions referred to in the report.

Authors
This report was written by Sue Nelson and Muhammad Saghir
Landis McKellar, the Evaluation Team Leader, provided editorial and methodological advice and quality assurance. Ms. Aurélie Ferreira was Evaluation Manager and Mr. Eric Tourres Project Director at Transtec.

Table of Contents

I. EXECUTIVE SUMMARY 1
II. INTRODUCTION AND DEVELOPMENT CONTEXT 4

I. Executive Summary

(i) Project Data

The Narrowing the Gender Gap in Flood Affected Areas of Pakistan project sought to reduce gender disparity and gender-

The project developed and used a Gender and Governance Performance Scorecard (GGPS) to monitor governance and service delivery and Short Message Service (SMS) cell phones to receive reports on corruption and violence against women (VAW). Community members marked the scorecards for five quarters and the findings were discussed with local officials in quarterly GRC district meetings. The SMS reporting generated reports on services, corrupt practices as well as VAW. Pattan aggregated the data for both efforts which was discussed at the GRC meetings with public officials. However, resolving these issues required more than sharing the information with officials, and without follow up most of the problems remained unresolved.

The use of inputs was consistent with the delivery of the activities but not with the intended outcomes. That would have required more continuity with the communities after workshops and with officials on the findings of the GGPS and SMS reporting. The GRC structures were

- **Lessons learned** as the project reporting showed the project had taken a synergistic and successful approach to gender issues in marginalized areas.

In addition, the team assessed the issues raised by UNDEF:

- **Effect of the project on men** as well as women as men were also included in the training and participated in the project-created structures.

iii.

working class women are employed in the informal sector, and earn less than a dollar a day.[11]

7KHUH LV VRPH OHJLVODWLRQ DGRSWHG WR SURWHFW ZRPHQ Criminal Law Act of 2009, but the application of laws is uneven and the police and the judiciary need training on their provisions and enforcement.

A 2005 World Bank study notes that ³JHQGHU JDSV LQ D FRXQWU\¶V SROLWLFDO economic dimensions are intertwined with the FRXQWU\¶V RYHUDOO GHYHORSPHQW that increased economic opportunities for women and gender parity are essential for economic development and for Pakistan to achieve its Millennium Development Goals.[12]

This is a mid- to long-term endeavour the Bank reports will need political, economic and cultural changes. In the near term, the study notes that women need access to services and opportunities. This requires active policies to promote gender equality, eased constraints on women and girls including their access to basic services, paid work and opportunities for decision making in the public space. It also requires changing the cultural norm of restricted female mobility, where the safety of women and girls in the public space is a family preoccupation. ThisThik H8(hi)69(sch533.o0 0 1 7)6(k)-10(ti)5(on)3(i)5(t)BT 1c [(d)] TJ ET BT 1 0 312048

IV. Evaluation findings

(i) Relevance

The p

Figure 2. GRC Membership

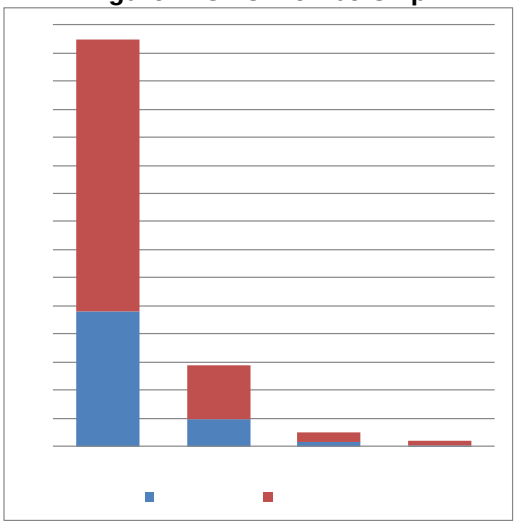

members in Nowshera however, who had a higher educational level, were clearer on their role and understanding of the issues. However, Pattan still drove these structures. As an example, local officials named the project staff rather than the GRC members when discussing the GRC V¶ activities.

Figure 3. GPPS Scorecard

The GRCs did engage in several continuing activities. One of these was the GGPS scorecards. This was a way to monitor public services and problems in the communities and increase citizen voice and engagement. About 150 - 200 scorecards per district were distributed quarterly for five quarters. About 85 percent of the cards were returned each quarter which was a good return rate. The data was aggregated and analyzed by project staff.

Figure 4. SMS sheet with codes to report incidents

Findings were discussed in the GRC meetings, primarily at district level, with relevant officials. Some of these were large meetings as initially 26, and eventually 40, institutions were monitored (Figure 4). Some GRC members felt the groups were too large and the time for discussion too short to be able to address the findings. Nevertheless, this effort increased the official V ¶ awareness that community members were grading the quality of their work and services and this process increased the visibility of problems. GRC members felt that the officials tried to be responsive although they could not provide examples of any specific actions taken as a result of the cards. These quarterly meetings appeared to be the extent of the advocacy activities done by the project beyond a few GRC follow up visits to schools, clinics and other institutions, and to Pattan publishing the information on its website.

Main issues reported through SMS

- Absent teachers 19%
- Forced to pay bribes 18%
- Absent doctors 12.6%
- Girls kept from school 10.8%
- + R V S L W D O V G R Q ¶ W J L Y H I
- Violence against women 4.7%
- Forced to vote for candidate 4.08%

Although the score cards were completed by both men and women, the cell phones were only distributed to some of the most active female GRC members. This was controversial as mainly men had phones in these areas (57 percent vs. five percent for women according to the baseline survey). Project staff again approached the men to gain their approval and couched the tool in terms of it being only able to send SMS messages to report governance and corruption problems rather than to make regular calls or to report only on violence against women.

The phones were programmed with codes so that if the user pushed a specific number it would register a complaint about a particular issue (Figure 5). A large number of the phones were not used even though the project provided training on the phones (Figure 6). The reasons given were that they were difficult to use and had a short battery life. However, the phones did allow for the women to safely report problems. Pattan reported receiving 2,701 complaints. About two-thirds of these were on poor governance, and a third was on violence against women.

Figure 5. Number of cell phones distributed and used

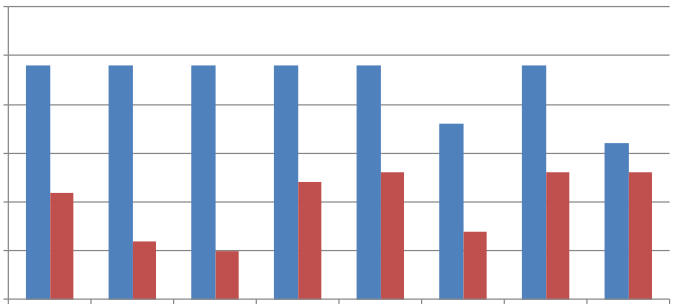

Figure 6. Planned vs. Actual Participation in Workshops



(iii) Efficiency

The project inputs were consistent with the delivery of its outputs, but not with W K H S U R M H F W ¶ intended outcomes. To achieve these, more follow-up efforts would have been needed with the GRCs and communities. The GRC structures should have also allowed for a much more decentralized and efficient execution of the project than the in/out type of implementation done by visiting project mobilizers. That would have allowed for a more consistent delivery over time and the strengthening of these local level structures.

Pattan seemed well organized and experienced in project management. It put good project management and monitoring systems in place. It quickly recruited project staff with a good deal of experience, and who had worked with Pattan on other projects. Project staff met seemed qualified and commitment to the work. They were clear on their roles, on the project approach and on its activities. Pattan developed a comprehensive Project Implementation Manual and trained project staff on the project as well as on project reporting and accounting procedures. It required social mobilizers to give weekly travel plans against which it provided weekly advances. All of this helped to ensure consistency in their work and adherence to the implementation plan. It also helped to ensure that Pattan was able to collect the information it needed to manage the project and report on it in a complete and timely manner. All of the project products were we

equipment and print media.
The project had a complete monitoring and evaluation (M&E) plan. Pattan documented its work and had put systems in place to collect the information from the field, review it and report on it from its main office. This included a comprehensive base line survey done in all target areas that provided qualitative as well as quantitative knowledge, attitude and practice (KAP) data on the communities and their residents. This information was used to guide the selection of communities and trainings as well as to provide a baseline against which Pattan could measure project results. The impact survey undertaken at the end of the project was not the same type of survey and used focus group discussions that repeated only a small number of the baseline questions. The focus group discussions provided more anecdotal information that did not allow for the needed comparisons with the baseline data to determine impact.

Some of the indicators chosen also only measured project outputs rather than results, and some of its targets were unrealistic. For example, the target for Outcome 2- improved progress towards MDGs was a 70 percent increase for women and 20 percent for men in the number of persons registered to vote. However, their baseline data showed that 80 and 90 percent respectively of persons were already registered. End of project reporting also did not report on the achievement of the target and instead discussed the work of the project on the topic.

(iv) Impact

The impact of this project is difficult to assess despite the wealth of data collected by the grantee for the reasons already noted. Information beyond outputs is limited. The differences between the questions and methodology used for the baseline and impact surveys make comparisons between the before and afters of the project difficult. The lack of continuity of the project within the communities and the limited role of the GRC also reduced the potential for impact which is evident in some of the discussions provided in the focus group report.

Nevertheless, the project worked in extremely disadvantaged and isolated communities and the interaction of project participants with project staff and each other on important issues of equity, civil registration, and political participation and on basic health and education issues, had to have affected some of the individual lives of participants and in some cases, within the broader community. This is evident in the 17 short case studies done by Pattan at the end of the project.

Some of the project issues are also those addressed by other CSOs and government agencies, especially in the lead up to a national election, so attribution of results in some cases to this project would be difficult. The impact on women can be expected to be greater than it was for men in general as the women were the main focus The

right to an education for all, the right for women to have health care, the right to vote for the candidate/party of your own choice, the right to have accountable officials and service delivery and the right to report corruption and violence against women.

- Increased confidence of women and some m ale participants . The information and awareness raised at the community levels was empowering for some participants. This was visible in the impact and case study reporting where some women stuck up for themselves when facing intimidation and/or denial of their rights by male family members and others. It was also visible in the interviews when participants discussed rights issues such as schooling, birth registrations, CNIC registration and the right for women to vote. They had no hesitation in answering these issues during the interviews.

- Provided a support mechanism for men and women who were harassed or denied their rights through the creation and training of the GRCs. In the harsh circumstances for women in some of the project locations, the GRCs provided safety in numbers for some men and women to make complaints and/or have them taken seriously by authorities. In some cases, the GRCs met with the problem persons and/or officials to try to help resolve the issues. In several cases Pattan had to bring in press and legal support to address the problems.

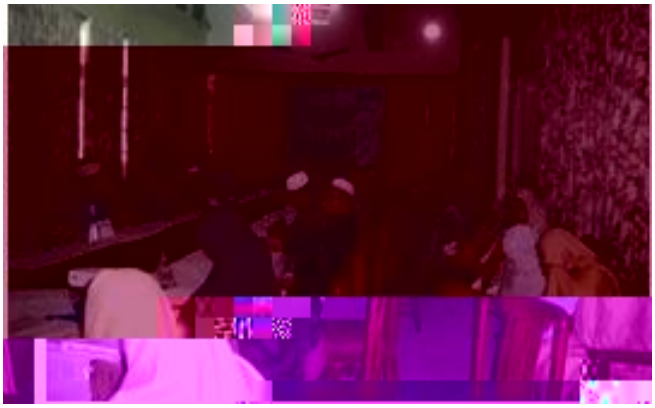

Meeting in Swat on GGPS findings, Photo: Pattan

- Built support for girls ¶enrollment in schools

,I sdel sdlated to birth and CNIC reggr

)LJXUH :RPHQ¶V PDQLIH

IV. Conclusions

Based on the evaluation findings, the team concludes:

(i) The project provided important and needed information on rights and issues of gender equity that directly affected the lives of the persons within the targeted communities. The project areas were marginalized and notorious for the way women were treated. It is highly unlikely that these communities would have focused on civil and political rights issues, and especially for those related to gender, without projects such as these. This

V. Recommendations

To strengthen similar projects in the future, the team recommends:

(i) Ensure sufficient follow up for activities . Quarterly visits are not enough to develop a dynamic project capable of making transformational change. Grantees should ensure there is regular contact with

(vi) GRC structures should be more fully developed and given a leadership role in the project. For the next project, implementation should be delegated to the decentralized structures created by the project. The GRCs should be developed into bodies capable of managing the efforts within their geographic areas and be delegated the responsibility and resources needed to do this work. Project staff should guide the process, providing the materials, serving as resource persons and filling a quality control role rather than directly implementing every activity. GRC leadership positions should have educational requirements as well as integrity and impartiality criteria so that they understand the issues and their role and are perceived within their areas as civic leaders. This recommendation follows conclusions (i), (ii), (iii), (iv), (v) and (vi).

(vii) More thought should be given in the setting of targets and indicators that can more accurately capture the results of the project. The same questions should be repeated between surveys so that the differences in knowledge, attitude and practices can be compared as this is where project impact will be found for a project such as this. This recommendation follows conclusion (vii).

VI. Overall assessment and closing thoughts

These types of projects are extremely valuable because of the depth of need and level of inequities for women in Pakistan, especially in the areas targeted by the project. Working in these areas on issues such as democratic values and gender rights is not an easy task. Villagers are not always welcoming. Many do not understand democratic concepts and think democratic strengthening projects are part of a larger foreign agenda intended to destroy their way of life. It is also difficult to discuss rights when there are other pressing issues within these very poor communities, such as security, Taliban extremism and a need for basic necessities such as schools, shelter, livelihood, health, drinking water and sanitation.

The bones of this project were very good. But the synergistic program outlined in the Project Document was too ambitious to implement without better use of the decentralized structures created. ' H Y H O R S L Q J W K H V H O R F D O V W U X F W X U H V that could continue to meet and follow up on community issues with officials should have been at the heart of this design. The GGPS scorecards and reporting through SMS were key tools in these efforts. These gave the information needed to systematically monitor the performance of their local government and services providers as well on specific problem areas, such as VAW and corruption. These issues transcend the gender aspects of the project and monitoring and addressing them can empower whole communities.

VII. ANNEXES

Annex 1: Evaluation questions:

DAC criterion	Evaluation Question	Related sub-questions
Relevance	To what extent was the project, as designed and implemented, suited to context and needs at the beneficiary, local, and national levels?	ƒ Were the objectives of the project in line with the needs and priorities for democratic development, given the context? ƒ Should another project strategy have been preferred rather than the one implemented to better reflect those needs, priorities, and context? Why? ƒ Were risks appropriately identified by the projects? How appropriate are/were the strategies developed to deal with identified risks? Was the project overly risk-averse?
Effectiveness	To what extent was the project, as implemented,	

Annex 3: Persons Interviewed

16 June 2014	
National Expert travel to Multan	
17 June 2014	
Mr. Shahid Waseem	Manager Accounts & Admin, Pattan, Multan
Ms. Banjamin Barkat	Program Manager, Pattan, Multan
Mr. Mushtaq Chishti	District Coordinator, Pattan, Multan
Mr. Ghulam Yasin	Social Mobilizer, Pattan, Multan
Mr. Mahmood Ramzan	Social Mobilizer, Pattan, Multan
Mr. Pervez	Community Mobilizer, Pattan, Multan
Ms. Rida-e-Zanab	Project Assistant, Pattan, Multan
Ms. Samia Arif	Community Mobilizer, Pattan, Muzaffargarh
Ms. Nasim Jehan	Community Mobilizer, Pattan, Multan
Ms. Kausar Hussain	Community Mobilizer, Pattan, Layyah

Travel to Islamabad	
18 June 2014	
Mr. Adnan Chughtai	Manager Finance Administration, Pattan, Islamabad
Mr. Muhammad Ismail Khan	Manager Accounts, Pattan, Islamabad
Ms. Rabia Ghani	Project Coordinator, Pattan, Multan
Ms. Aysha Adil	
Mr. Kamran Shafi	

Annex 4 : Acronyms

CBO	Community Based Organization
CNIC	Computerized National Identity Card
GGPS	Gender and Governance Scorecard
GRC	Gender Reform Committee
KAP	Knowledge Attitude and Practices
M&E	Monitoring and Evaluation
MDG	Millennium Development Goals
NADRA	National Database and Registration Authority
NGO	Non-Governmental Organization
SMS	Short Message Service
UNDEF	United Nations Democracy Fund
USD	United States Dollar
VAW	Violence Against Women
