Evaluation of the Peacebuilding Fund (PBF) Project Portfolio In Somalia

Evaluation Report

27 December 2019

Evaluation Team:

- Dr. Terrence Jantzi (Team Leader)
- Anara Alymkulova (Peacebuilding Specialist)
- Mohamed Adnan (National Context Specialist)

KonTerra Support:

- Erisa Yzeiraj Pereira (Research Analyst)

Strategy (2018), the Wadajir framework for Local Governance (2016) and the National Development Plan (2017). In Somalia, the PBF portfolio is a relatively small proportion of all peacebuilding funding aligned with these frameworks. The overall annual investment for peacebuilding in Somalia varied between US$243 million - US$271 million annually

connection between the larger investment environment and the specificities of the portfolio gaps targeted. In terms

that connected separated communities; and, iv) the formation of local committees with diverse representation for oversight, monitoring or project steering.

19. For youth, the supported projects have been positive in their inclusion of youth into community processes (SOMD1 Midnimo); peacebuilding and dispute resolution skills (IRF-152 Kenya-Somalia cross border); and in access to economic opportunities (SOM-D1 Midnimo, IRF -152 Kenya-Somalia cross border, SOM D2 Daldhis). However, the number of youths that were affected by the programming is a relatively small proportion of the total youth population. For gender outcome, there has been observed increases in womenís participation as a result of the projects, but less progress in womenís representation in decision making bodies or Governance. For example, women

and appropriate application. The IRF-120 Risk Management Unit and the IRF-141 National

26. Perhaps the one catalytc effect that was not freq

funds allocated through the portfolio were recorded as being spent in line with their budget forecasts. Only three projects reported achieving fewer than 90 percent of their targeted outputs (SOM-D2 Daldhis, IRF-143 Coor

to ensure good delivery and coherence of the fund. There are challenges with strategic oversight of the fund itself through this mechanism.

35. Strategic level respondents are able to verbally articulate the strategic coherence of the individual gap-oriented projects and are able to articulate their linkage to the larger strategic frameworks present in the context. However, this conceptualization of a gap-oriented portfolio is not well captured in existing documentation. Project reports on individual projects and evaluations of individual projects are the responsibilities of the

	US$6 million , Youth ï US$2 million , Rule of Law ï US$5 millio n)
PBF/SOM/D -1: Midnim o (Unity)	Yes. During implementation, the United Nations Trust Fund for Human

(approvals within days). Implications for disbursement of funds, accountability, and reporting would need to be modified, hence the

23 percent of all girls in Somalia attend primary education and 87 percent of girls and women are illiterate. These factors are exacebated among internally displaced women and children who are often subjected to gender-based violence and abuse and a high presence of unaccompanied minors.[25] The country is preparing for universal suffrage elections in 2020/21, the first since a military coup in 1969. The election has the potential to contribute to consolidating peace gains.[26]

5. According to a study done by the Overseas Development Institute (2017), the New Deal Compact has contributed to key results such as the reengagement of the International Financial Institutions (IFIs), and supporting the process of obtaining debt relief.[27] With the introduction of the New Deal Compact, the Federal and regional governments have taken increased ownership of assistance-related decision-making and a larger share of international resources have been channeled through national systems.[28] The Compactôs principles have served as afoundation for the establishment of the Somalia Development and Reconstruction Facility (SDRF), a centerpiece for the partnership between the Somalia government and the international community. [29] Additional barriers still exist for peacebuild

role and strengthening the linkages between it and its citizens is critical for the peacebuilding process in the country.

- Supporting local reconciliation processes - The absence of a functional justice system and undermined customary mechanisms for dispute resolution such as court or traditional courts, and customary laws contributed to a disruption of the reconciliation component of the peace process. The second pillar of the PPP emphasized supporting the strengthening of both formal and traditional justice systems to strengthen local reconciliation processes through a multi-stage process prioritizing the inclusion of all citizen stakeholder groups.

- Inclusive economic and social growth - Somalia has one of the highest youth unemployment rates in the world, which has exacerbated vulnerabilities, especially among youth (and women). One factor for increased feelings of disenfranchisement and unrest among youth is considered to be the lack of economic development and opportunities. This can lead to engagement in non-legal alternatives or to increased radicalization. Economic development and social growth were considered important within the PPP to mitigate potential conflict drivers and increase resilience to economic and natural shocks. Women face additional barriers to economic and political inclusions ranging from cultural norms to lack of education access and property rights.

- Building the capacity of the Government at local and Federal levels - The years of [illegible]

committee is responsible for providing overall strategic guidance and coordination between the Government, the United Nations in Somalia and the PBSO.

PBF Portfolio Theories of Change

17. The PPP developed in 2016 aimed to ñestablish strong state-citizen links, based on community resilience and recoveryefforts that are supported by responsive state institutions, to achieve the dual aim of providing peace dividends and strengthen trust in the political transitionò.[38] To achieve this goal, the PPP elaborated an overarching ToC to serve as a guiding framework. All the projects under the PBF portfolio of support have their own ToC, which contribute directly to the PBF global priorities. The PPP ToC was tre W* 0 595.32 841.92 re

community engagement, presenting an effective model of operation that brought practical solutions, security and access and others. Each Recipient United Nations Organization (RUNO) either jointly or individual would develop the idea for a project or programme and then present a project concept paper. The justification for the concept was linked to one of the four global PBF Strategic Priority areas. During the period covered by this evaluation, the PBF portfolio of support was operationalized through 17 projects. Eight IRF projects concluded within the evaluation period and are included in the evaluation. The two PRF projects, SOM-D1 Midnimo and SOM-D2 Daldhis[39], have recently been completed (in August 2019) and are included in the scope of the evaluation. Additional projects which commenced in 2018 or later are not included in the evaluation. The following Table 2 lists the 10 projects included in this evaluation[40] and Figure 1 depicts their chronology within this period of support.[41]

Figure 1: Chronology of Projects under Review



		government funds and foreign aid that comes in the country through promotin g fiduciary accountability, conflict sensitivity and informed decision making for portfolio management and capacity development.
Second Phase (approved in 2016/2017)	PBF/SOM/D -2: Daldhis (Build	

23. First Phase: IRFs developed in 2015/2016. These IRF projects were built outside and before the frame of the Peacebuilding Priority

27. The SOM-D1 Midnimo programme was designed as a new programme focusing on implementation in the two newly established States The SOM-D1 Midnimo operationalized Outcome

3. Determine the catalytic effects of PBF's support to Somalia and assess fundraising strategies by implementing partners and the PBF;
4. Assess where the critical remaining peacebuilding gaps in Somalia are;
5. Assess whether the peacebuilding interventions funded by the PBF successfully contributed to promoting the women's, peace and security agenda as set out in United Nations Security Council Resolution 1325;
6. Provide

Effectiveness, and Sustainability questions).[48] The

10. Facilitating cascade effects where indirect impacts have a multiplier effect from PBF support.

39. The evaluation matrix in Error! Reference source not found. describes in detail these categories, key questions, the judgment criteria, data collection methods and analysis methods. The matrix is intended to serve as the foundation of the evaluation process and dictated the structure in the final report, including conclusions and recommendations. All other inquiry tools, such as interview guides (Semi-Structured Guides in Annex 5), are oriented towards it. Cumulatively, the evidence available against each question/performance indicator should enable a response to the relevant evaluation question.

2.2 Evaluation Methodology

40. The evaluation matrix is linked to the PPP logic model, specifically through its judgement criteria, which were elaborated based on the intended results, organizational processes and expected social change. The evaluation drew on both qualitative and quantitative measures. The quantitative measures were obtained from pre-existing documentation including project reports and evaluations and are associated with the individual project logframe indicators. Qualitative data was (r)-2(gan)6(i)] TJ ET Q q 0.000008871 0 59

Figure 2: Field Visit Locations – Evaluation Team[50]

42. Data Analysis: The ET reviewed together the range of responses from stakeholders for each element in the matrix and employed a standard qualitative approach of an iterative analysis of emergent themes.[51] Key thought units were identified in interviews. These were then clustered into categories and emergent themes from each category were identified for further analysis and re-categorization to identify key patterns.

43. Evidence for conclusions was built via triangulation analysis.

PPP outcome level indicators that had been elaborated at the time of the design and the absence of other reliable outcome indicators whose values could be attributed to the PBF portfolio of support (described further in the findings section). Neither the SOM-D2 Daldhis nor the SOM-D1 Midnimo project re 11.04 Tf 1 0 0 1 368.47 761.28 Tm 0 g 0 G [(th)-7(e)5( )] TJ ET Q

Neither t

3.1 Relevance , Results and Contributions

3.1.1 Relev ance

49. Relevance add

throughout the current PBF cycle.[53] Annually, the PBF portfolio represents roughly 5 percent of peacebuilding funding in any given year; reportedly ranking 17th among all the donors in Somalia during a donor review in 2018. Due to the relatively small ñfootprintò of the PBF portfolio in the country and due to the existence of highly elaborated peacebuilding frameworks with articulated conflict drivers already present, the PBF portfolio has, with the exception of the SOM-D2 Daldhis and SOM-D1 Midnimo PRF projects, taken a ñgap-orientedò approach to the support of peacebuilding projects; identifying opportunities to support a diverse range of projects that address gaps in the support provided by the larger donors and investments to peacebuilding in the country. Even though there is considerable peacebuilding investment, the need still outweighs the available funding in specific arenas and the PBF can play an important role in targeting these specific dimensions. When overlaid against the backdrop of the larger strategic frameworks, the gap-oriented approach is appropriate and strategic for the context

52. One of the implications of a gap-oriented approach is that the exercises of identifying a theory of change in a PPP or exercises for identifying conflict drivers generated valid and relevant drivers and ToCsï but they were to a certain exte

of support ï such as the area based intervention logic, or that it was an innovative project, or that it was a joint programme experiment between two Agencies that had not worked together previously rather than to the conflict driver or ToC itself that was in use.

National Development Plan. However, at the operational level and within the operational documents, more descriptions could be found of actions oriented towards gender and youth sensitivity in programming . This

75. A compiled analysis from all of the individual projects does not fully capture the contributions of the projects to higher level results even though the output and outcome

Reconciliation Conferences						
PBF/IRF -116 S2S						
PBF/IRF -120 Risk Management						
PBF/SOM/D - 2: Daldhis						

Parliament is a woman. [57] Although there has been more funding and investment in narrowing the gender gap, the positions and findings from the IRF-119 Womenîs Political Participation project which ended in 2016 are still the same positions put forward by the Somalia Women Parliamentarians in 2019, including: [58]

1. Increasing womenîs representation to 30 percent of Parliamentary seats
2. Mainstreaming Gender Responsive Budgeting
3. Promotion of women to refrain from engaging in clan-based conflicts
4. Increasing Womenîs representation in national and regional decision making forums [59]
5.

en to refr

87. In contrast, United Nations respondents tended to describe systems and legislation and processes ï the establishment of courts, or District councils ï and to emphasize the quality of the inter-relationships between the different levels of Government (Federal, State, District). Respondents from the higher levels of the United Nations system also d

donors.[60] Establishing mechanisms for channeling funds through national Government to local levels was also seen as high risk by donors but was supported through the IRF-120- Risk Management Support and the IRF-141National Window projects. The PBF was seen as one of the mechanisms for being able to work within these higher risk situations that were often not available to other donor instruments. Many respondents perceived this work through the PBF/IRF-141 National Window as pioneering ï moving into uncharted territory ï and ap

Governance, and Youth Empowerment[64]) were all examples of pre-existing programmes that had received ñtop upò funding from the PBF. H

portfolio of support[66] and all of the UNCT Agencies engage in one or another of these elements which are contributing to peacebuilding in the context. The Government stakeholders also use these areas for formulating their National Development Plan and Wadajir National Framework for Local Governance. The stakeholders are already involved in supporting the peacebuilding Agenda through alignment with and engagement in these national level frameworks for peacebuilding in Somalia.

103. What was cited in the interviews and observed during the field mission were examples of increased inclusion of new Agencies in the PBF portfolio and increased inclusion of stakeholders in the processes from citizen level mobilization in SOM-D1 Midnimo through District level authori

	project design and portfolio coordination? 7. (Daldhis and Midnimo only): How timely and cost efficient were the implementation of the Daldhis and Midnimo projects.

106. Efficiency of Projects. Efficiency in the implementation of individual projects is usually assessed through a comparison of the output level indicators achieved in the projects against planned targets and in cost efficiency through a comparison of budget to expenditure. These two efficiency measures are summarized in the Table 8 below. The data is abstracted from the end of project logframes and reports. Projects often underwent substantial shifts which were not always captured in the logframes and reports. In some cases, the amount of reported expenditures differs among data sources. Table 9 provides additional details on funding and spending and notes when there are discrepancies in funding reporting.

Table 8: PBF Portfolio Efficiency Measures

Project	Percentage of Output Indicators Meeting Targets	Percentage of Funds Spent
PBF/SOM/D-2: Daldhis (Build Your Country) - An integrated approach to re-establish the State-Citizen link in Jubbaland and South West State of Somalia	62%	78%
PBF/SOM/D-1: Midnimo (Unity) - Support for the Attainment of Durable Solutions in Areas Impacted by Displacement and Returns in Jubaland and South West States	93%	40%
PBF/IRF-116 Support to the Federal Government of Somalia in Stabilization in Newly Recovered Areas (S2S)	92%	92%
PBF/IRF-120 Risk Management Support for the UN MPTF Somalia and Somalia Development and Recovery Facility (SDRF)	100%	100%
PBF/IRF-152: The Kenya-Somalia refugees and peacebuilding cross border pilot project for voluntary return, co-existence and sustainable Reintegration in the areas of return (SOMALIA)	100%	76%
PBF/IRF-122 Support for Somalia Reconciliation Conferences	97%	94%
PBF/IRF-121 Somalia Joint Rule of Law Programme - Justice and Corrections Support	33%	90%
PBF/IRF-141 Pibt Project to Strengthen Service Delivery Through Federal Government Systems in Federal Member States and Interim Regional Administrations	100%	94%
PBF/IRF-119 Strengthening women's role and participation in peacebuilding - Towards just, fair and inclusive Somalia	92%	100%
PBF/IRF-143: Coordination Support for the Implementation of the Peacebuilding Priority and Measures to Pilot Studies of Public Response to Peace and State building Efforts in Somalia	69%	100%
Total	80%	71%

Table 9: Project Expenditure Rates

Project Title	Duration	Budget Approved (in US$)	Total Budget Spend (in US$) [67]	Percentage Spent [68]
PBF/SOM/D-2: Daldhis (Build Your Country) - An integrated approach to re-establish the State-Citizen link in Jubbaland and South West State of Somalia	14/12/2016 - 31/08/2019	5,300,000	4,11	

PBF/SOM/ D-1: Midnimo (Unity) - Support for the Attainment of Durable Solutions in Areas Impacted by Displacement and Returns in Jubaland and South West States	14/12/2016 - 31/08/ 2019	4,500,000	1,787,156.76 (annual report 2018)	40%
PBF/IRF-116 Support to the Federal Government of Somalia in Sta				

108. Documentation can be misleading regarding under-reporting of indicators. For example, the IRF-121 Somalia Joint Rule of Law received PBF funding to ñjump startò implementation on a pre-existing programme

113. The formation of District Councils was one of the key fulcrums of the Local Governance programme and the programme could not deliver funding for infrastructure rehabilitation until the District Councils had become established. Therefore, significant downstream funding was predicated on the achievement of this first activity. The establishment of the District Councils were not as easy to set up in the newly established States as anticipated. In addition to access and security constraints, the competing political interests among the different Governance levels,

two modalities, but it is even more interesting to consider the elaboration of a modality that might be sufficiently responsive to a political orientation. There has been experimentation with building a flexible response fund into existing projects in the Third Phase of the [illegible] and there was a similar fund within at lea

132. Strategic level respondents are able to verbally articulate the strategic coherence of the individual gap-oriented projects and are able to articulate their linkage to the larger strategic frameworks present in the context. However, the existing programme documentation, and the associated PBF M&E, does not currently capture the coherence, logic, or contributions to impact sufficiently. This can present challenges both for supporting institutional memory during transitions but also for demonstrating ñvalue for moneyò to donors. The PBSO s

require faster responsiveness or a [redacted] donor sources. These approaches are logical options give[redacted]tions M&E ï while a programme oriented approach can[redacted]olio [redacted]is substantively more challenging to provide M&E at [redacted]vel for [redacted]

137. Individual project outcome i[redacted] to be compiled individually. Contex[redacted]ch as the CRE[redacted] potential mechanism for identifyin[redacted] changes in the con[redacted] capture the effects of the entire s[redacted]ilding interventions rather than just the portfolio interventions. The change[redacted]uld be more likely to be the results of the larger peacebuilding framework an[redacted]g rather than the specific ñgapò projects within that larger framework.

138. Furthermore, smaller proofs[redacted]r strategic innovations philosophy would further limit the ability of these la[redacted] see the specific contributions of smaller projects. These datasystems have [redacted]f or use in guiding decisions on large scale programming, geographic prioritiz[redacted], [redacted] assess the results of the entirety of peacebuilding programming in Somalia, but would not be able to disaggregateor different iate the much smaller ï albeit strategic ï components supported by

142. For example, there is already a risk assessment matrix managed by the PBF to assess the riskiness of the project. he PBF to assess

providing oversight on the portfolio. However, in the context of Somalia, this body has been limited in its oversight of the PBF oversight due to access and security conditions. It is very difficult and expensive to organize events that bring both Government and United Nations representatives together. There is also a concern that there are already a very large number of coordination meetings already present in the context ï for much larger resources. The stakeholders from Government or the United Nations often are the same persons on many of these bodies. Convening extremely busy high level officials for duplicated events has been a concern in Somalia. As such, the approach has been to attempt to integrate PBF oversight into pre-existing coordination spaces. Respondents cited many different bodies when a

this analysis: i) Government ownership; ii) Community-Based Mobilization; iii) Social Cohesion; iv) Integration and Coordination; v) Aspirations and Capacity; and vi) Timeliness.

establish the State-Citizen link in Jubbaland and South West State of Somalia	x Ensuring adequate representation of clan interests

152. Government ownership. The inclusion of Government ï preferably multiple levels from Federal through Local authorities ï in project design and to take the lead in implementation produces significant positive effects. This had not been the normal practice for most of the external interventions in the context and as noted earlier in the narrative, was a highly valued component of project implementation by Somali stakeholders.

153. Community-Based Mobilization. Much of the programming to support the extension of State authority is perforce moving from higher levels towards communities. However, there is a significant need to balance this top-to-bottom approach with efforts that begin with community-based mobilization and engagement that can interact with these top-down extensions. Projects that included grassroots mobilization components were seen as providing a positive contribution to fill a gap in other donor supported

funding from differen

Government - that involves multiple Ministries in collaboration with each other - which should include joint monitoring as well as operational coordination.

4 Conclusions and Recommendations

4.1 Conclusions

168. The portfolio has contributed to the achievement of higher-level results. The most significant results have been related to i) solving inter-clan disputes, negotiations, and grievances; ii) developing administrative and financial systems for accountability and to facilitate inter-level coordination; iii) supporting the creation of basic governance infrastructure for the delivery of services at sub-national levels, and iv) increasing community engagement. The six major contributions of the collective portfolio have been to: i) delivery of basic services; ii) improved social cohesion; iii) increased Federal/State/District cohesion; iv) enhanced community and District mobilization for development; v) improved mechanisms for Rule of Law and settlement of grievances; and vi) improved economic opportunities.

169. Due to the logic of using the portfolio to address strategic gaps in the larger pre-existing frameworks and to respond to emergent priorities, the measurement of these results is based mostly on qualitative assessments. The contributions have been distributed across a wide range of potential themes given the diversity of the projects under review. Although gap-oriented, the PBF portfolio integration into discussions with the UNCT, political Mission and Government has allowed the PBF projects to contribute to the broader strategic objectives of the national development plan by filling gaps in programming. The PPP PRFs SOM-D1 Midnimo and SOM-D2 Daldhis are both seen to have contributed important strategic outcomes in the SWS and Jubbaland states. SOM-D1 Midnimo is seen as the more successful of the two projects primarily for two reasons: a) the response time to see changes at community levels are much faster than for enacting changes in Government processes;and b) the integration of portions of three separate national level joint programmes into a more localized SWS and Jubbaland context in SOM-D2 Daldhis underestimated the degree of contradictions and complexities in project steering and coordination.

170. An enormous variety of catalytic effects were cited by respondents – primarily by the Unit

173. Efficiency of the individual projects is generally good for the context, with the exception of the SOM-D2 Daldhis project due to the aforementioned joint programming coordination challenges and the difficulties in the establishment of the District Councils. The efficiency of the portfolio management was perceived differently by different stakeholders.

179. From an implementation perspective, significant challenges are presented due to limited institutional memory and transitions of personnel. Further efforts on knowledge management, knowledge sharing, or stakeholder integration into best practices from the fund could be helpful in future programming .

4.2 Recommendations

180. The ET would recommend another cycle of PBF support. The suggestion would be

4.2.2 PBF Systems, Management and Coordination

185. Recommendation 5 - Political Responsiveness: For the next cycle, PBSO should consider piloting adaptations to existing modalities that might allow for better fit to the political agenda in terms of responsiveness and timeframe. This could be either an adaptation of the IRF or the elaboration of a

5 Annexes

5.1 Annex 1: Statement of Work

Statement of Work for
(1) Team Leader/Evaluation Specialist (2) Peacebuilding Specialist and (3) Country Specialist for
Evaluation of the Peacebuilding Fund (PBF) Portfolio in Somalia (2015 - 2019) [84]

1. INTRODUCTION

The PBF, established in 2005 through General Assembly resdution 60/180 and Security Council resolution 1645,

implementation as a resut of security and political developments and have had to request for extensions.

Strategic role of the PBF in Somalia

The PBF has contributed to positioning the UN at the forefront of peacebuilding and state-building efforts in S

o

After ten years of PBF support to Somalia and in the final year of implementation of the 2016-2019 Peacebuilding Priority Plan, a final, independent evaluation of the PBF's investments in Somalia is requested by PBSO's Senior Management. This will be the first comprehensive portfolio-level evaluation of the PBF's investments in Somalia, which is a requirement for renewed PBF eligibility. This evaluation is therefore timely, as it presents an excellent opportunity to assess the PBF's achievements and overall added value to peacebuilding in Somalia. It will also contribute to a better understanding of the effectiveness of the PBF's strategic decision-making, its alignment with national frameworks and the UN's political mandate in Somalia, implementation modalities and partnerships, and finally whether the PBF has successfully leveraged its role as a catalytic, innovative and risk-

members of the UN Country Team in Somalia. It will also serve as relevant inputs to the PBF policies and guidance, and other corporate-level reviews.

The evaluation findings and recommendations will be used to inform actions to further strengthen key aspects of the PBF's current and future work. The recommendations should be actionable and on how the PBF and its partners can improve their effectiveness. The final report will be a public document.

- To what extent did the PBF and the Peacebuilding Priority Plan respond to urgent funding needs and/or peacebuilding relevant gaps?
- To what extent was the PPP informed by contextual changes, joint conflict analysis, and lessons learned following PBF's pre-2015 investments in Somalia? To what extent did they have strategic coherence?
-

- How fast and responsive has the PBF been to supporting peacebuilding priorities in Somalia?
- What role did the PBF Coordination Committee play in ensuring efficient use of PBF's investments?
- How efficient was the implementation of the PBF support and how significant were the transaction costs?
- What role did the PBF Secretariat in the RCO play in support of the project design and portfolio coordination?
- Overall, did the PBF investments provide value for money?
- To what extent were the resources programmed in an efficient and strategic manner, including the selection of implementing partners?
- How well did the M&E system work?

- To what extent did the PBF portfolio from 2015-2019 achieve higher-level results?
- To what extent did the PBF support take risks to achieve peacebuilding objectives, especially in areas where other donors were not ready to do so?
- How strategic was the Peacebuilding Priority Plan at seizing important political opportunities for greater peacebuilding impact and creating catalytic effects?
- To what extent did the PBF projects contribute to the broader strategic outcomes identified in the Peacebuilding Priority Plan?
- To what extent did Dhaldhis and Midnimo, as flagship projects under the Peacebuilding Priority Plan, complement each other a

- How strong is the commitment of the government and other stakeholders to sustaining the results of the PBF support and continuing any unfinished activities?
- What, if any, catalytic effects did the PBF support in Somalia have (financial and non-financial)?
- Did the PBF-funded projects generate gender- and age-disaggregated data through its M&E approaches to inform new programming?

Following from the overall assessment, the evaluation will assess the relevance, efficiency, effectiveness and sustainability of the PBF's total contribution to Somalia during 2015-2019, including under two outcomes of the Peacebuilding Priority Plan. Examples of types of questions to be considered to examine this strategic, substantive contribution are provided below:[86]

x *Outcome 1: Government structures and institutions at federal, regional, district and community level are strengthened, more accountable and transparent and better able to listen and respond to the various needs of populations in the new*

Evaluatio

- How efficient was the partnership with Government counterparts in the design and implementation of PBF-funded projects?
- How relevant was PBF's support for achieving national strategic priorities?

To what extent did the PBF projects contribute to overcoming political challenges by bringing different stakeholders closer together?

- How effective was the support provided by the PBF/PBSO (including PBSO in New York and the PBF Secretariat) to the Recipient United Nations Organisations (RUNOs) and Non-UN Organisations (NUNOs)?

0.00000912 0 612 792 re W* n BT /

The Peacebuilding Specialist should possess the following skills and expertise, at a minimum:

- Masterôs degree in a relevant area including social sciences, international development, conflict studies, law, or public administration;
- Five to seven years of post-conflict/peacebuilding experience, including experience in peacebuilding programming design and implementation;
- Demonstrated understanding of conflict analysis, conflict drivers and post-conflict recovery;
- Demonstrating understanding of political, human rights, governance and/or reconciliation issues;
- Demonstrated understanding of gender issues and women and peacebuilding;
- Experience in working with government officials, international development community and people recovering from conflict;
- Demonstrated familiarity with the United Nations and its Agencies, Funds and Programmes;
- Excellent written and oral communication skills, including in cross-cultural contexts;
- Strong teamwork skills; and
- Fluency in English, while knowledge of Somali is desirable.

The Somalia Specialist should possess the following skills and expertise, at a minimum:

- University degree in a relevant field, including social sciences, history, conflict studies, etc.;
- Five years to seven years of relevant work experience, including experience working in Somalia;
- Excellent knowledge of Somaliaôs cultural, political and socio-economic context with a focus on post-conflict recovery;
- Knowledge of Somaliaôs governance institutions and existing contacts in those institutions, facilitating teamôs communication and analysis of the stakeholders/beneficiaries of the PBF programme;
- Understanding of past and current state of political, human rights, governance and reconciliation key issues in Somalia;
- Experience in research 0 612 792 re W* n BT /F2 11.04 Tf 1 0 0 1 343.15 613.9 Tm 0 g 0 G [(n)15(

overvi12 0640-g4038n0 6138n85.8T TJ ET Q q 0aia Sp

Deliverable	Content and Audience	Tentative Due Date
	consolidated matrix of comments which should	

Lis t of pr ojects to be e valuated

Pro ject ID	Project Title	Duration

5.2 Annex 2: Pr oject Summaries

5.2.1 Over all Summary

Name of Proje ct	PBF (Global) Priori ty Area/ OUTCOM ES	RUNOs	Partn ers	Location	Orig inal Bud get Approv ed	Du ra tion [88]

PBF/IRF-122 Support for Somalia Reconciliation Conferences	Priority 2 - coexistence and peaceful resolution of conflict Focus Area 2.1 - National Reconciliation	UNDP	UNSOM, Ministry of Interior, Federal Affairs and Reconciliation, Regional Admin of Jubbaland State, Interim South West Admin, Galmudug Interim Admin, Banadir, Regional Admin of HIraan and Middle Shabelle	Galkayo (Galmudug and Puntland states), Dhusamareeb and Adaado (Galmudug), State of Hirshabelle, Marka, Jowhar	$2,598,173	15/09/2015-30/04/2017
PBF/SOM/D-1: Midnimo (Unity) - Midnimo (Unity) - Support for the Attainment of Durable Solutions in Areas Impacted by Displacement and Returns in Jubaland and South West States	Priority 2- coexistence and peaceful resolution of					

Key Challenges, Milestones and/or Lessons learnt (annual report, eval etc)	x The PBF secretariat, through the coordination fund, has supported the

Key Challenges , Milestones and/or Lessons lea rn t (annu al repo rt)	The achievements are very much at activity

5.2.2.3 PBF-SOM D1 – Midnimo

Project Name	PBF/SOM/D-1; Support for the Attainment of Durable Solutions in Areas Impacted by Displacement and Returns in Jubaland and South West States(00103708)
Project Start date	14/12/2016
Project Duration (end date)	31/08/ 2019
Implementing Office	IOM, UN-HABITAT
Implementing Partners	Government: -Jubaland Refugee andIDP Agency for Jubaland State; Ministry of Planning & International Coordination for South West State
Implementing locations	Jubaland Kismayo, Garbarharey, Afmadow and Dollow and for South West State - Baidoa and Afgoye
Funding	Original budget: $4,000,000; Final budget with other additions:US$ 4, 500,00 0
Target Beneficiaries	Returnees, IDPsand Host Communities. Formation of: Community action groups (CAGs) and community-basedmonitoring and evaluation committees (CBM&Es), Community-based local dispute resolution committee(CBDC)
Outcomes	Outcome 1: Government structures and institutions at Federal, regi ET Q q 65f 1 0 0 1 421.63 544.6

Catalyti c Effect	1-Financial leverage
Project Description	This proposed programme aimed to enhance local leadership capacities to facilitate the sustainable return, recovery, social integration and peaceful co-existence of displacement affected, returnee, other migrant groups and host communities in Jubaland and South West State. The project is Government-led and community-driven to ensure a bottom up approach todrive transition and recovery processes in displacement affected communities. The Midnimo project is intended to promote stability in fragile and displacement affected areas of Somalia, as well as theattainment of durable solutions to internal displacement. ( )
Evalu ation Findings	x Changes in geographic scope of project, and increase in funding x Unlike any other project, the Midnimo concept evolved to include federal government, local authorities and federal member states directly into the project to take the lead in implementation. The project is implemented by government, hostcommunities and displaced communities, who prioritize activities, and during the prioritization process, asenseof trust and community cohes

solutions strategies and priorities into Federal Member State (FMS) and national peacebuilding, conflict resolution, anti-poverty and other transitional and development plans such as the recently presented FMS Stabilization Priority Plans in Somalia.

- CBP is a gender-inclusive and rights-based approach that advances IDPs and returnees participation in public affairs, at all levels, on an equal basis with the resident population. At the same time CBP meets obligations of relevant legal standards including in particular: international human rights, international humanitarian law, the African Union Convention for the Protection and Assistance of Internally Displaced Persons in Africa and the Guiding Principles on Internal Displacement.

- The Midnimo approach contributes to [illegible] capacity building, government led and community driven efforts through existing planning and development[illegible]

5.2.2.4 PBF/IRF 152: Kenya Somalia

Evaluation Findings	x

5.2.2.5 PBF/IRF -141: National Window

Project Nam e PBF/IR F-141Pilot Proj ect to Strengthen Service Delivery Through Federal

	x There are some limitations in measuring public perception due to safety concerns x Irregular flight schedule to project locations especially Garbaharey and Hudur districts of Jubbaland and x Southwest states respectively have also contributed to the delays in project implementations.

5.2.2.6 PBF/SOM -A2: Nationa l Recon cilia tion Conferenc es Support

Pro ject Name	PBF/IRF -122 ï Support to Somalia Local Reconcili ation Processes
Project Start date	15/09/ 2015
Proj ect D urati on (end date)	30/04/2017
Implem enting Of fice	UNDP
Impl ementin g Partners	UNSOM, Mini stry of I nterior , Federal Affairs and Reconciliation, Regional Admin of Jubbaland State, I nteri m South West Admin, Galmudug Interim Admi n, Banadir, Regional Admin of Hi raan and Midd le Shabelle
Imple menting l ocat ions	Galkayo (Galmudug and Puntland states), Dhusamareeb and Adaado (Galmudug), State of Hi rshabelle, Marka, Jowhar
Fu n ding	$ 2,232,061
Targe t Ben eficiaries	
Outcomes	Out come 1: Outcome 1: Support the FGS with facilita ting reconcil iation towards state formation / The

5.2.2.7 PBF-IRF-120: Risk Management Unit

Project Name	PBF/IRF-120- Risk Management Support for the UN MPTF and SDRF Somalia
Project Start date	

Key Challenges, Milestones and/or Lessons learnt (annual report, eval etc)	Lessons Learnt x Sustained risk management to joint programmes and crossUN x Agencies has enabled collective response to contextual, strategic and operational risks and increased donor confidence in UN in Somalia ad renewed donor support x PBSO support to both MPTF risk management and National Window pilot project has enabled the synergy between the MPTF risk management and capacity development of government institutions as MPTF fund recipients and implementers under the national window.\ x The use of National Window supported by a strong and sustained risk management focus is an essential element of the UN support to the extension of Federal and State Authority and accountability as it enables programmes to take measured risks to expand their delivery beyond Member State capitals. x Risk Management and Use of Country systems are two areas that have

5.2.2.8 PBF/IRF -121: Joint Rule of La w

Project Name	PBF/IR F-121Somalia Joint Rule of Law Programme - Justice and Correcti ons Support
Pro ject Start date	31/08/2015
Pro ject Duration (end date)	31/08/2 016
Implementing Office	UNDP, UNOPS, UNODC, UNICEF
Implementi ng Partners	Ministry of Justi ce, Supreme Court
Implem enting locat ions	Federal Somalia and IRAs, Puntland and Somalil and
Fundin g	Ori ginal budget: $2,143,821
Direct Benefi ciarie s	Insti tutio ns at FGS and FMSlevel (e.g. The Judicial Trai ni ng Center), Attorney General Offices, lawyers, tradi tional justi ce actors, Police Force, and people with no access to legal services.
Out comes	OUTC OME 1 [90]: Establish independent and accountable justice insti tuti ons capable of addressing the justice needs of the people of Somalia by delivering justice for all.
	Out come

[90] The outcomes and outputs listed here are based on ProDoc. Different (additional) out comes are listed in the annual report

Evaluation Findings

- JROLP has been too broad and over-ambitious, without capturing the essence of what it wanted to achieve.
- Program has an over-emphasis on capacity building the criminal justice system, at the expense of strengthening the civil law legal system. Need to invest more in the judiciary and the Attorney Generals Offices.
- Donors are choosing increasingly to work bi-laterally with UN entities due to the expensive additional costs of the MPTF and administration that is involved. JROLP needs to demonstrate and reiterate the viability and relevance of the in-country MPTF programme structure to donors and national stakeholders, as well as work on a cohesive aid delivery platform
- Lack of clarity about ójointnessô and meaning of óRoL,ô modalities to use and poor coordination among PUNOs which resulted in duplication of activities
- Short, medium and long-term planning for sustainability, as well as exit strategies appear to be largely absent
- There is a lack of clarity (e.g. a Road Map) setting out an agreed basis for how the informal and formal justice systems will develop and what the interface between the two will look like
- Programmes are highly relevant and have a broad reach, having contributed to development of future justice stakeholders and entities
- Unrealistic expectations on the Programme are sometimes due to circumstances outside its control; better Somali coordination is needed and more fluent and consistent funding from donors.
- UNODC should either scale down its scope and ambitions in Somalia, or sigted TJ Ee 0 f[(t)] TJ ET Q

5.2.2.10 PBF/ IRF -119: Stre ngth ening Wome n's Role in Peacebuilding

Pr oject Na me	PBF/IRF -119- Strengthening women's role and participation in peacebuilding - Towards just, fair and inclusive Somalia
Pro ject Start date	13/07/2015
Project Duration (end date)	31/12/2016
Imple men ting Offi ce	UNDP, UNSOM, UN Women
Implementing Partner s	Gov ernme nt: Mi nistr y of Women and Human Right s Development (MoWRH D - Federal) Mini stry of Women Development and Family Affairs (MoWDAFA - Puntland) CSOs: Somali Women Leadership Initia tive (SWLI) , others to be determi ned through competitive bidd ing. Re searc h ins tituti on: Heritage Institute for Poli cy Studies
Implem enting locat ions	Mogadishu (Federal), Puntland, Baidoa, Kismayo, Geddo, newly emerging states and recovere

Evaluation Findings	x The Project had a moderate performance in terms of expected results, with different levels depending on the Outcome. A general consideration is that the focus of the action was placed more generally on participation of women in politics arena, and not so much in the specific thematic of peacebuilding and state building x Proposed intervention in political representation and participation are very high level and hard to achieve in such a small (and short) project. Design seems cohesive with the context; M&E not systematic; x Overall project needed to define better its contribution (e.g. capacity building or advocacy re the New Deal gender inclusion etc) and its direct impact. The successes were produced because of joint efforts with other initiatives working towards the same purpose x Much of the changes have been operated top to bottom. There have been progresses at a higher level, but those changes must be accompanied and sustained by the society. x The internal structures of coordination and joint articulation did not work and in practice. Constituted more a separation of financial resources and programmatic roles. Weak collaboration with the UN structure of the joint programme and the partners x The Project did not consider a sustainability (social, financial, or operational) strategy. However, some activities in the programming and practices in the implementation conducted to that direction
Key Challenges, Milestones and/or Lessons learnt (annual report, eval etc)	x Milestones: x 24% women representation in parliament (higher than the African average for women's parliamentary representation; hope for inclusive politics x The progress in the Policy and Legal reform has reached important milestones: GBV Policy, Gender Policy, FGM Policy, SOB, Constitutional review, CEDAW ratification x The project played a catalytic role in securing a grant from DfID for $5.6million to build on the PBF project achievements and focusing on women's enhanced political leadership and empowerment. x A focused and coordinated action between all the different social, institutional and international cooperation agents is an effective and efficient approach in a complex context, with many factors against it and with limited resources. It was demonstrated with the lobby for the 30% of seats for women in Parliament. A focused intervention, in the frame of a wider strategy, is a proper strategy to produce small changes inside a bigger agenda.

5.3 Annex 3: PPP and Individual Project Results Frameworks and Summaries

5.3.1 Individual Project Logframe Output and Outcome Indicators

Table 3.1- First Phase Project Outcome Indicators by Priority Area [92]

PBF Priority Area 1. Support to Implementation of Peace Agreements and Political Dialogue			
Indicator	Baseline	Targets	End line
PBF/IRF-121 Somalia Joint Rule of Law Programme - Justice and Corrections Support			
# of gender-responsive police related institutions or internal units established with UN support	n/a	1	2
# of cases fully adjudicated in the mobile courts (disaggregated by criminal (rape and SGBV and other) and civil cases (e.g. womenôs socio-economic rights and other), and dismissals and convictions, and district) (and sex) / age)	n/a	50	574
# of strategies, SOPs, Code of Conduct, or systems that are gender-responsive and meet human rights standards developed or revised in support of justice sector institutions (disaggregated by: institution, and type)	n/a	2	1
PBF Priority Area 2. Promote coexistence and peaceful conflict resolution			
Indicator	Baseline	Targets	Endline

Priority Area 4 : (Re-)build essential administrative services and infrastructure			
Indicator	Baseline	Targets	Endline
PBF/IRF-116 Support to the Federal Government of Somalia in Stabilization in Newly Recovered Areas (S2S)			
Value in ($) of resources expended by district administration	$10,000 per district	10 districts expended $ 28,000.00	$150,500 total for 12 districts
# of coordination meetings between			

# of youth aged 15-24 enrolled in certified livelihoods training	0	750	803
# of persons of concern (18-59) with own business/self-employed for more than 12 months	0	750	803
# of returnees recorded and tracked in PRMN as successfully integrated and co-existing well with host communities	0	1500	1402
PBF/SOM/D-2: Daldhis (Build Your Country) - An integrated approach to re-establish the State-Citizen link in Jubbaland and South West State of Somalia			
Number of youth (% women) employed in self-or wage-employed in Baidoa and Kismayo		0	94 youth (38 women) got longer-term jobs
Number of public infrastructures rehabilitated in Baidoa and Kismayo		2	2

Number of youth (% women) got short-term jobs in rehabilitation works in Baidoa and Kismayo

5.3.3 PPP Theory of Chan ge

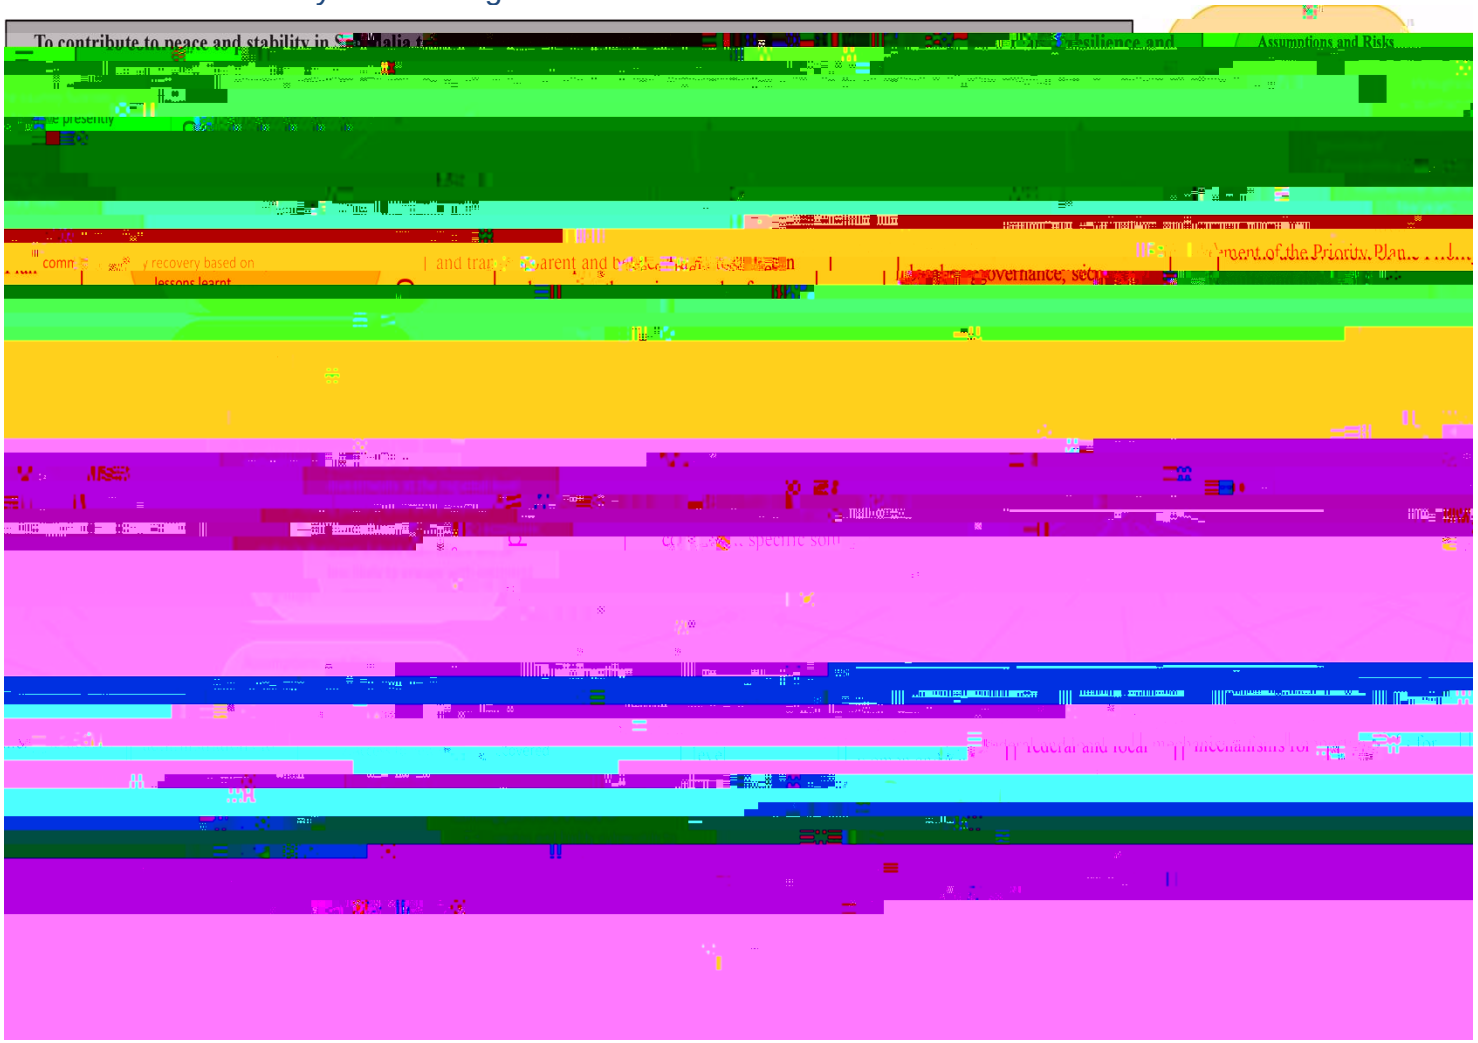

5.3.4 P

of institutions or units that receive procured equipment disaggregated

# of strategies, SOPs, Code of Conduct, or systems that are gender-responsive and meet human rights standards developed or revised in support of justice sector institutions (disaggregated by: institution, and type)	N/A	1 (outreach material package)	Delayed
# of people reached by awareness campaigns (disaggregated by provider, topic, sex and district)	N/A	1000	Puntland ï 350 (M:265, F:85)

# of Programme Steering Committee M

# of legal aid centers supported (disaggregated bytype and district)	N/A	12 legal aid centers	Hargeisa University Legal Clinic with 2 Legal aid offices and Head Office at Hargeisa University Faculty of Law and the Office in front of the Hargeisa courts
# of gender-responsive justice sector institutions or internal units established with UN support	N/A	1	2 institutions (AGO and the newly established Women and Child Units).
# of people reached by awareness campaigns (disa			

# of justice sector professionals trained (disaggregated by sex, topic, districts and type of professional such

# of strategies, Policies, SOPs, Code of Conduct, or systems that are non-discriminatory and meet human rights standards developed or revised in support of SLP (disaggregated by: institution and type)	N/A	2 Documents: (Staff audit report; Biometric registration strategy)	Delayed
Comprehensive Training Programme for Police tested and finalized	N/A	56 modules tested and finalized 1 new module developed on SGBV investigations	Delayed
# of police trained (disaggregated by sex, topic, districts and rank	N/A	Trainers – 25; Officers -120 (pilot phase) Officers - 150 (Phase 1 roll out) Manuals - 500	Delayed
# of Police trained (disaggregated by sex, topic, districts and ranks	N/A	450 (F:150; M:300) Refresher – 100; Trainer mentor - 25	Delayed
# of individuals that have received scholarships	N/A	30 Officers (M:22, F8)	Scholarships – 30 (F:8; M:22)
# of strategies, Policies, SOPs, Code of Conduct, or systems that are non-discriminatory and meet human rights standards developed or revised in support of SLP (disaggregated by: institution and type)	N/A	3 Documents (Buildings needs assessments; Communications; and Transport)	Delayed
# of institutions or units that receive procured equipment (disaggregated by district, type and recipient)	N/A	1 unit (6 vehicles)	Delayed
# of police related institutions or units established with UN support	N/A	1 (SOP Police Planning Unit)	Delayed
# of police related institutions or units established with UN support	N/A	1 MOI Police Reform Team	Police Reform Team reactivated
# of strategies, Policies, SOPs, Code of Conduct, or systems that are non-discriminatory and meet human rights standards developed or revised in support of SLP (disaggregated by: institution and type)	N/A	10 Policies (SOPs drafted and approved by the government)	4 -SL Strategic Plan; -Police Monitoring Plan; -Community policing training handouts; -Guidelines on assessment for SL Police
# of institutions or units that receive procured equipment (disaggregated by district, type and recipient)	N/A	0 (Baseline to be established through Capacity Assessment)	Delayed
Number of Programme Steering Committee Meetings	N/A	N/A	N/A

5.3.5 PBF Priority Area 2. Promo te coex iste nce a nd peaceful conflict resol uti on

5.3.6 PBF Priority Area 2. Promote coexistence and peaceful conflict re soluti on[97]

PBF/IRF -119 Strengthenin g womenôs role and participati on in peacebuilding - Towards just, fair and inclusive Somalia

The project strengthens womenôs role and agency for the advancement of their po litical empowerment and direct ly supports the gender equality commitment s made by the Federal Government of Somalia in the framework of the Somali New Deal Compact. The project aims to strengthen the capacity of CSOs advocating on women participation as well as to bring a gender focus in the national government stru ctures.
Im

community problem solving (disaggregated by sex)			
# of technical advisors/officers (TA/Os) and interns provided to BFC to assist in policy development and implementati			

Coordination for South West State			
Performance Indicators	Indicator Baseline	Target	Endline (incl. latest annual report)
Output Indicator 1.1.1. Number of district and/or community level government representa			

Output Indicator 1.6.1: Framework document agreed upon with the relevant authorities and stakeholders	0	1	1
Output Indicator 1.7.1: Number of final draft terms of reference aligned with the Regional Constitution ready for approval	0	1	1
	0		
Output Indicator 2.1.1: Number of individuals participating in community based planning processdisaggregated by gender and socio-economic status	n/a	1200	[redacted]

perceptions of their physical safety and security			
Output Indicator 2.5.1 Number of community advisors hired per pilot project site	0	1	1
Output Indicator 2.5.2 Number of projects selected by communities are submitted to the advisors	0	24	28
Output Indicator 2.6. 1: Number of committees trained	0	6	2
Output Indicator 2.6.2: Number of training sessions held	0	9	2
Output Indicator 2.7.1: Number of community meetings held per target site	0	18	2
Output Indicator 2.7.2: Number of community selected projects are supported by technical advisors and finalized	0	4	0
Output Indicator 2.7.3: Number of mixed use settlement areas identified by communities and authorities for small scale resettlement	0	2	1

Indicator 1.1 # of returnees trained in peacebuilding and conflict resolutions and are participating in democratic governance and reconciliation processes	0	750	626
Indicator 1.2 # of youth aged 15-24 enrolled in certified livelihoods training	0	750	803
Indicator 1.3 # of persons of concern (18-59) with own business/self-employed for more than 12 months	0	750	803
Indicator 1.1.2 # of returnees trained in peacebuilding and conflict resolutions.	0	750 (3000)	626
Indicator 1.2.1# of persons provided with entrepreneurship/ business training.	0	750	803
Indicator 2.1 # of persons benefit. The Indicator Based Performance Assessment from social services provided in newly resettled areas	0	3,000	4,387
Indicator 2.2 # of returnees recorded and tracked in PRMN as successfully integrated and co- existing well with host communities	0	1,500	1,402
Indicator 2.1.1# of persons benefit. The Indicator Based Performance Assessing from social services provided in newly resettled areas	0	3,000	4,387
Indicator 2.1.2 # of returnees recorded and tracked in PRMN as successfully integrated and co- existing well with host communities	0	1,500	1,402
[redacted]dicator 2.2.1 # of children attending primary school.	0	1,800	1,863
[redacted]dicator 2.2.2 # of teacher training and incentives	0	75	60

monitoring tool to measure the satisfaction of citizens with the rehabilitated infrastructures		implemented by the PIU and IRA/State authorities and PIU and the UN	
Indicator 1.1.1 % of people (men and women) expressing trust in targeted Federal Member States	43%	80%	67% of the residence are confident with the district administration according to OCVP report.
Indicator 1.1.2 Number of infrastructures built and functional	0	4	4
Indicator 1.2.1 Number of Public Service Announcements are aired on popular radios in target locations where infrastructures are being rehabilitated/constructed	0	7	7
Indicator 1.2.2 PIU Facebook page	0	Min. 3 posts per week during project implementation n At least 1000 likes by the end of the project	24 Facebook post had been made and 6,613 likes for the entire project duration.

I

through Trust Fund that proactively manage risks of gender equality and women's empowerment			All joint programmes have mainstreamed gender targeting 30% of beneficiaries are women. Gender indicator has become a mandatory requirement for all joint programmes.
Indicator 1.3.2 Percentage of Trust Fund resources allocated to gender specific activities/interventions	13%	20%	Targeted achieved. RCO and UN Women have introduced gender indicator in the progress reports to ensure proper monitoring of the gender related activities with sufficient resources, having a direct and indirect impact on gender empowerment.
Indicator 1.3.3 Percentage of projects implemented through Trust Fund that syst			

Implementing Office : UNDP, JPLG (UNDP, UNICEF, ILO, UNCDF, UNHABITAT), UNIDO Implementing Partners : Federal Government of Somalia: MoIFA, MoPublic Works, MoJustice, MoF, Federal Member State (Jubbaland/SWS): Mo Interior, Mo Justice, MoEducation, Mo Labour and Employment, MoTrade and Industry			
Performance Indicators	Indicator Baseline	Target	Endline (in cl. latest annual report)
# of decentralization or local govemance related policies that are developed or drafted and gender sensitive	0	2	2
# of decentralization or local governance related legislation/ sector specific policies, including fiscal decentralization developed (or drafted) and gender sensitive	0	4	4 (two adopted by SWS andJS. 2 drafts by HS and GS)
# of coordination and oversight meetings	0	6	12
# gender sensitive policies, guidelines and policies issues for effective coordination and oversight of the activities.	0	2policies drafted (FGS- SWS and FGS ï JBL)	0
# of formal mechanisms of coordination that exist at Federal and states level	0	2 (FGS- SWSand FGS ï JBL)	2
# of districts that have systems in place to increase revenue generation (eg property taxes, business licensing etc)	0	8 (South West and Jubaland)	0
# of monitoring visits completed by state governments staff to district level governance bodies	0	Target: 8 (1* 4 quarters*state governments of SW and JB- 1*4*2). It is minimum required number of visits.	1
1: No. of Mobile Training Units established. 2: No. of trainings delivered by the Mobile Training Units. 3: No. of target participants trained by the Mobile Training Units.	0	4	3 training teams in 2017 0 in JL and SW trainings expanded to other FMS in 2018
# of CSO and NGOs that are part of the dialogue with local government/ authorities.	0	at least 50% of those present in South West State and Jubaland	0
# of socioeconomic issues constructively discussed in the dialogues with local government/ authorities (Suggested- employment, health, education, social infrastructure, youth and etc)	0	TBD	0
# of local and central government personnel trained in at least one PEM module	0	TBD as per training plans	206 100 in Jubaland, 106 in SWS

# of district council members trained in civic education, public management, procurement.	0	TBD as per training plans	30 in Hudur SWS
Number of cases fully adjudicated by the mobile courts (disaggregated by criminal (rape and SGBV and other) and civil cases (e.g women's socio-economic rights and other), and dismissals and convictions, and district) (and sex) / age)	1,231 cases adjudicated in 2016	Increase in adjudication by 25%	Total: 345 Å South West: 23 (22 civ, 1 crim) F:8 and M: 15; Å Jubaland: 55 (42 civ and 13 crim) F:18 and M:37;
Number of youth (% women) trained in civic education and life-skills for social rehabilitation and economic reintegration in Baidoa and Kismayo	n/a	200 youth at risk (100 from Baidoa and 100 from Kismayo) at least 30% women	200 youth (46% women) Total 404 youth Number of youth (% women) employed ï self-or wage-employed in Baidoa and Kismayo 0 94 youth
Number of youth (% women) employed ï self-or wage-employed in Baidoa and Kismayo	n/a	0	94 youth (38 women) got longer-term jobs
Number of public infrastructures rehabilitated in Baidoa and Kismayo	n/a	At least 2 public infrastructures	2
Number of youth (% women) got short-term jobs in rehabilitation works in Baidoa and Kismayo	n/a	0	118 youth (30 women) in Kismayo and Baidoa by creating 9,204 workdays

5.4 Annex 4:

No.	Key Question: To what extent did the PBF portfolio as a whole from 2015-2019 achieve higher level results?	Data Tools	Data Analysis Modules
1.0	To what extent are Government structures and institutions at Federal, Regional, District and Community Level strengthened, accountable, and transparent so as to better be able to respond to needs of the population?	x Document Analysis Exercises x Semi-Structured Interview Guides National Stakeholders/External Observers Implementing Partners	

development, and promoting increased economic opportunities	1.4.5 Citizens assess state capacity for delivery of services to be enhanced

No.	Sub-questions	Judgment Criteria	Data Analysis Modules
3.1	To what extent has PBF portfolio of projects been successful to leading to increased well-being?	3.1.1 State institutions support measures to improve participation in public life 3.1.2 Creation of peace dividends: Sustainable economic development opportunities for marginalized groups (IDPs, youth, women, returnees) are created 3.1.3 Reintegration and rehabilitation of ex-combatants 3.1.4 Citizens have a positive disposition toward others	
3.2	Among the projects within the PBF Portfolio of support, what were key factors for success?	3.2.1 Project reports and evaluations highlight lessons learned 3.2.2 Project RUNOs can cite success factors in projects in PBF Portfolio 3.2.3 Community and Government stakeholders can cite positive success factors	

Daldhis and Midnimo Observations			
No.	Key Question	Data Tools	Data Analysis M

No.	Key Question		
8.0 How effective and efficient were the arrangements in-country and between PBSO/PBF and the UNCT for PBF Portfolio Management			
No.	**Sub-questions**	**Judgment Criteria**	**Sources**
8.1	How well did the management processes with the PBF/PBSO provide good support to the PBF Portfolio?	8.1.1 Decision making processes transparent 8.1.2 Decision making processes efficient 8.1.3 Decision making processes led to good decisions 8.1.4 Approval processes timely	PBF Portfolio Process Consolidation Document Synthesis
8.2	To what extent did the JSC processes include high degree of ownership and diverse engagements	8.2.1 Government Leadership Strength 8.2.2. Civil Society Representation 8.2.3 Stakeholder dhip	

MIA x UN/virtual Skype interviews (Team together)	MIA x UN/virtual Skype interviews x Government stakeholders Interviews	MIA x UN/virtual Skype interviews Baidoa x Government stakeholders Interviews x UN/NGOs Interviews	MIA x UN/virtual Skype interviews Baidoa x Government stakeholders Interviews x UN/NGOs Interviews	MIA x UN/virtual Skype interviews	MIA x UN /Virtual Skype interviews Hurdur x Potential Thematic FGDs x KIIs with govtstakeholders	MIA x UN/virtual Skype interviews Hurdur x Potential Thematic FGDs x KIIs with Govt stakeholders
13-Oct	14-Oct	15 ï Oct	16 ï Oct	17 ï Oct	18-Oct	19-Oct
MIA x UN/virtual Skype interviews x Government stakeholders Interviews	MIA x UN/virtual Skype interviews Kismayo x Government Stakeholders x UN/NGOs	MIA x UN/virtual Skype interviews Kismayo x Government Stakeholders x UN/NGOs	MIA x UN/virtual Skype interviews Kismayo x UN/NGOs Dollow District x Potential Thematic FGDs x KIIs with govt stakeholders	MIA x UN/virtual Skype interviews Kismayo x UN/NGOs		

	Abdulkon Hassan Ibrahim	Ministry of Justice South West State, Admin/ Finance/HR Officer	Baidoa, 08/ 10/2019
	Abdusalam Osman	Ministry of Justice SWS, Senior Legal Officer	Baidoa, 08/10/2019
	Abdullah Asan Ibrahim	Ministry of Justice SWS, Mobile Court Coordinator	Baidoa, 08/10/2019
	Nasir Abdi Arush	Minister of Humanitarian Affairs and Disaster Management SWS	Baidoa, 08/10/2019
	Mohamed Maolin Isack	Board Member and former programme manager WARDO NGO/Daldhis project	Hudur , 09/10/2 019
	Suliyman Bashir Mohamed	Focal point man WARDO	

	Sadia Mohammed	Director of Gender, Ministry of Women.	10/10/2019
	Abdirahman Abdi Ahmed	DG Ministry of Interior, Jubaland	13/10/2019
	Ahmed Osman	DG, Ministry of Education, Jubaland	15/10/2019
	Abdirahman Barkadle	UN Habitat Programme Officer, Kismayo	15/10/2019
	Ben Mbaura	IOM, Durable Solutions Project Officer	15/10/2019
	Irfan Mahmood	Operations Specialis	

5.7 Annex 7: Pr o

negotiation skills so as to inform and
influence the PSG processes is inc

engagement and dialogue
with local

5.8

5.9 Annex 9: Data Collection Tools

5.9.1 Document R

5.9.2 Semi-Structured Guides

Semi Structured Interview Guides

These guides are designed to be a "semi-structured" interview guide

Semi Structured Interview Guide
Coordinating Committee [101]/PBF Secretariat

Section 1: PBF Portfolio Framework Development

1. What do you see as some of the main challenges and successes of the PPP or PBF Portfolio framework development phase? (4.1)

13. How responsive was the PBF portfolio of support to new challenges or barriers to implementation (4.3)
    a. What adjustment were made based onlessons learned

14. How did youion (4.3)

Gov er nment, C

3.

Imp lementing Par tners

To be us ed wit h stakehol ders who hav e been involved with a spec ific project

Section 1: Introduction

. What has been your role in this project? (if the project is a follow-up from a previous project, was he/she involved in

Section

District Council Stakeholders

Section 1: Introduction

1. What has been your role in the District?
    a. For how long?

2. Which projects do you remember being implemented for peacebuilding in this district?

3. How connected were you with any of these projects?

Section2: Development and Relevance

1. Would you describe the process that led to the development of the project/s? (4.3)
    a. How did you first hear about the projects?
        i. Inclusive?
        ii. Transparent
        iii. Government commitment

2. From your perspective, how relevant were the project/s in this District for achieving peacebuilding outcomes? (2.2)
    a. What were some gaps for peacebuilding that weren't being addressed by the project/s

3. How innovative did you see the project activities? (2.1)
    a. Originality /traditional

What types of catalytic effects have you seen from the projects being implemented in this municipality? (2.1)

a. Has the project catalysed additional support/commitment (political, financial)?
b. Has the PBF catalysed additional innovative programming adaptation
c. Networks as a platform for other peacebuilding?
d. Government commitment or changes
e. Innovative and Risk Taking Programming
f. Increased social cohesion and inclusivity

Section 6: Lessons Learned and Future Directions

1. What do you see as the most important lessons learned for building peace in this municipality? (3.0)

2. What do you see as the most important lessons learned for managing projects like these in the muni

The facilitator should write down comments around the causes noting successes, challenges, and why.

Note which projects were present in the municipality and which types of factors are being highlighted. Are some projects being mentioned more than others?

Step 5: After they have reflected on the community context, then the facilitator shou

5.9.4 Response Matrixes

Eval uation Resp onse Matrixes

Coordinat ing Commi ttee / PBF Secreta riat

Objective	Observ ations/N otes
PPP Development	
Operation ali zation of PPP	

Sust ainability	

s	

MUNICIPALITY Comparison (1.0, 2.1)	
Catalytic Effects (2.1)	

Evaluation Response Matrix
Provincial and District Representatives

Objective	Observations/Notes
Project Implementation	
